



Becker County Planning & Zoning
915 Lake Ave
Detroit Lakes, MN 56501
(218) 846-7314
www.co.becker.mn.us



Certificate of Compliance

Inspection Report - Permit #: SS2023-1788

Owner & Property Information

Owner Name:	BRANT R & PAULETTE L BEESON	Site Address:	13142 MERRY MEADOWS LN
Mailing Address:	BRANT R & PAULETTE L BEESON 13142 MERRY MEADOW LN DETROIT LAKES MN 56501-9805	Township - Sec/Twp/Rng:	LAKE VIEW - 16/138/041
Parcel #:	191465505	Legal Description:	Block 001 of MERRY MEADOWS 138 41 LOT 6 & EAST 40 FT OF LOT 7
Secondary Parcel #:		Designer:	Renner Excavating LLC, L2567 (Rick Renner)
		Installer:	Renner Excavating LLC, L2567 (Rick Renner)

Inspector Verified Specifications

Insp- Effluent Screen Installed:	No	Insp- Tank Nbr/Size:	1/1500/2
Insp- Alarm Required:	No	Insp- Drainfield Type:	Chamber Trench
Insp- Lift Pump in System:	No	Insp- Drainfield Size:	33 high capacity chambers X 15 square feet = 495 square feet
Insp- Number of Bedrooms:	4	Insp- Soil Verification:	#1: attached #2: N/A #3: N/A

Inspector Verified Setbacks

Insp- Tank Dist to Road	50	Insp- Drainfield Dist to Road	75
Insp- Tank Dist to Nearest Prop Line	50+	Insp- Drainfield Dist to Nearest Prop Line	50+
Insp- Tank Dist to Nearest Structure	15	Insp- Drainfield Dist to Nearest Structure	20
Insp- Tank Dist to Well	100+	Insp- Drainfield Dist to Well	100+
Insp- Tank Dist to OHW		Insp- Drainfield Dist to OHW	
Insp- Tank Dist to Pond/Wetland		Insp- Drainfield Dist to Pond/Wetland	
Insp- Tank Dist to Pressure Line		Insp- Drainfield Dist to Pressure Line	

Certificate of Compliance

(Yes) Certificate is hereby granted based upon the application, addendum from, plans, specifications and all other supporting data. With proper maintenance, this system can be expected to function satisfactory, however this is not a guarantee.

Certification Date: 08/14/2023

Zoning Office Signature:

Denise Gubrud

Denise Gubrud - ISTS Inspector

* Certificate of Compliance is not valid unless signed by a Registered Qualified Employee *

Field Review Form

Permit # SS2023-1788

Property and Owner

Owner: BRANT R & PAULETTE L BEESON

Parcel Number: 191465505

Site Address: 13142 MERRY MEADOWS LN

Secondary Parcel:

Home Information

Does the structure contain any of the following elements?

Designer submitted

Inspector verified

Garbage disposal: No

Dishwasher:

Grinder pump:

Lift pump in bsmt:

Garbage disposal? Y ☒ N ☒

Dishwasher? Y ☒ N ☒

Grinder pump? Y ☒ N ☒

Lift pump in basement? Y ☒ N ☒

Number of bedrooms: 4

Review - Number of bedrooms: 4

Effluent screen

Effluent screen installed? Y ☒ N ☒ Mfr:

Alarm: No Type: na

Review - Alarm? Y ☒ N ☒ Type & Mfr:

Lift pump in system: No

Review - Lift pump in system? Y ☒ N ☒ Mfr:

Component Information

Tank size: 1500

Review - Tank nbr: 1 size: 1500/2 Mfr: Inge/Hrator

Drainfield type: Chamber Trench

Review - Drainfield type: Chamber Trench

Drainfield size: Full size - 500

Reduced/warr. size - 500

Review - Drainfield status: none ☒ installed ☒ next spring

Review - Drainfield size:

Absorption area size:

Review - Absorption area size: 33x15 = 495 sq ft

Chamber type/num:

Trench sqft/chamber -

Review - Chamber type: Hi cap Num: 33

Review - Trench sqft/chamber: 15

Drainfield rock depth:

Review - Rock depth:

Soil Verification

Vertical separation verified

Boring #1:

Boring #2: attached

Boring #3:

Setback Verification

Distance to...	Designer submitted		Inspector verified	
	Tank	Drainfield	Tank	Drainfield
Road	45'	75'	50	75
Nearest prop line	50'	50	50+	50+
Nearest structure	15'	25'	15	20
Well	75	75	100+	100+
OHW	na	na		
Pond/Wetland	75	50'	50+	50+
Pressure line	50	50		


Date System Installed: 8/14/2023

Installer: Zack Penner

Inspector: Denise Gubert

1788

(N) Beeson

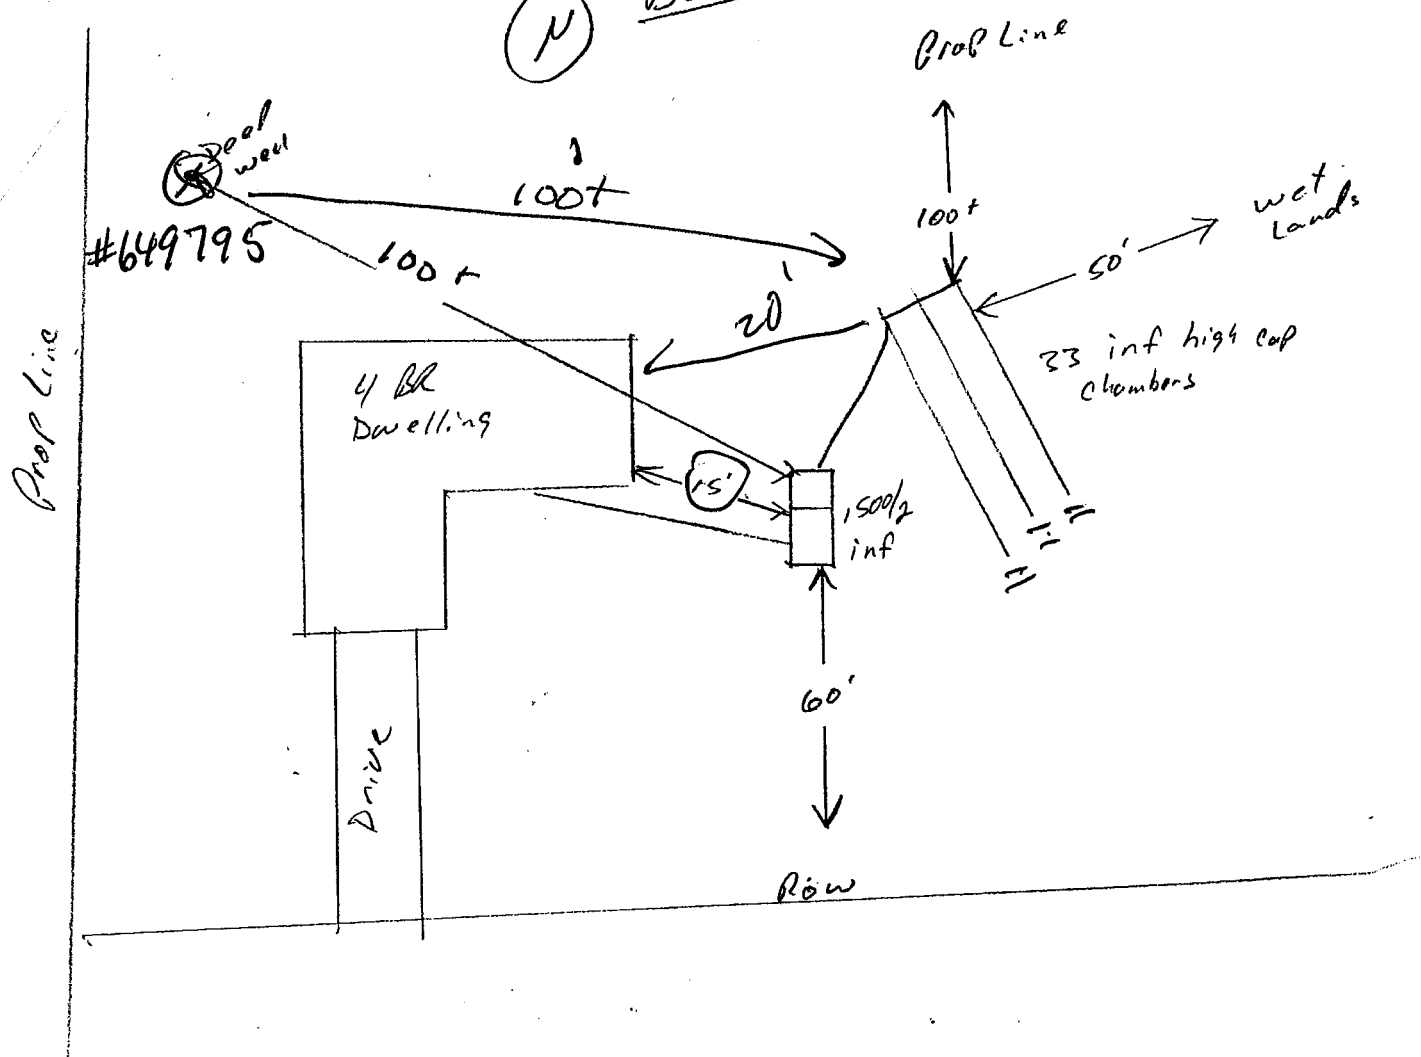

8/14/2023

1500/2 Infiltrator

33 Top fed Hi capacity chambers
setbacks & soils OK
Certify Denise Gutrud

Mike Beeson

Becker County Restrictive Layer Verification

Client: <u>Beeson</u>	Parcel: <u>191465505</u>	Date: <u>8-14-2023</u>
Address: <u>13142 Merry Meadows Ln</u>		
Vegetation: <u>lawn</u>		
Weather Conditions/Time of Day: <u>Sunny - noon</u>		
Depth (in)	Matrix Color(s)	Mottle Color(s)
84"	SL	none
Comments/Notes: 84" - no restrictive layer		

Certified Statement: I hereby certify that I have completed this work in accordance with all applicable ordinance, rules and laws.		
(Designer) <u>Rock Renner</u>	(Inspector) <u>Dewise Gubrud</u>	(Date) <u>8/14/2023</u>



Becker County Planning & Zoning
915 Lake Ave
Detroit Lakes, MN 56501
(218) 846-7314
www.co.becker.mn.us

8/14/2023

noon

Septic Permit

Permit #: SS2023-1788

Owner & Property Information

Owner Name:	BRANT R & PAULETTE L BEESON	Parcel #:	191465505
Mailing Address:	BRANT R & PAULETTE L BEESON 13142 MERRY MEADOW LN DETROIT LAKES MN 56501-9805	Secondary Parcel #:	
Phone #:	218-841-6221	Site Address:	13142 MERRY MEADOWS LN
Lake/River(1000/300):	No	Township - Sec/Twp/Rng:	LAKE VIEW - 16/138/041
Lake/River Name:	na	Designer:	Renner Excavating LLC, L2567 (Rick Renner)
Pond/Wetland(50):	Yes	Installer:	Renner Excavating LLC, L2567 (Rick Renner)


Specifications

Tank to be Installed:	Compartmented Tank	Type of Drainfield:	Chamber Trench
Total # Tanks Installed:	1	Full Size of Drainfield:	500
System Status:	Replacement System	Reduced/Warrantied Size:	500
System Serves:	Full-Time Dwelling	Absorbition Area Size:	
Number of Bedrooms:	4	Rock Depth:	
Design Flow/GPD:	600	Chamber Type and Number:	
Garbage Disposal?	No	Chamber Trench SqFt/Chamber:	
Size of Lift Pump:		Is System Pressurized?	No
Size of Lift Line:		Alarm?	No
Soil Sizing Factor:	.83	Type of Alarm:	na

Setbacks

Road Type:	Public / Township	Right of Way Marked:	No
Tank Dist to Road:	45'	Drainfield Dist to Road:	75'
Tank Dist to Closest Prop Line:	50'	Drainfield Dist to Closest Prop Line:	50'
Tank Dist to Nearest Structure:	15'	Drainfield Dist to Nearest Structure:	25'
Tank Dist to Well:	75	Drainfield Dist to Well:	75
Tank Dist to OHW:	na	Drainfield Dist to OHW:	na
Tank Dist to Pond/Wetland:	75	Drainfield Dist to Pond/Wetland:	50'
Tank Dist to Pressure Line:	50	Drainfield Dist to Pressure Line:	50

Other Information

Date Approved:	07/27/2023	Zoning Office Signature:	
Permit Fee:	\$225.00		
Receipt Number:	253179158		
Date Paid:	07/27/2023 8:16 AM CDT		
Notes: Install a 1500/2 septic tank and a chamber trench drainfield using 33 high capacity chambers			

PERMIT MUST BE POSTED AT JOB SITE. PERMIT EXPIRES ONE YEAR FROM DATE PAID.

** Please schedule for inspection prior to installation! **
